



ABANDONED MINE LAND INSPECTION

PROJECT NAME	PROJECT NO.	GRANT YEAR	REPORT NUMBER
Golden Pond Gob Removal	18302	2018	HNM0008705

CONTRACT INFORMATION		
CONTRACT NUMBER	EXPIRATION DATE	PERCENT OF CONTRACT COMPLETED
C196013	03/31/21	2
CONTRACTOR NAME		ENGINEER NAME
Russell County Reclamation, LLC		SCOTTY COX
SITE CONTACT PERSON: Kevin Large		

INSPECTION DATE	ARRIVAL	DEPARTURE	GROUND CONDITION
06/24/19	02:15 PM	02:45 PM	WET
06/19/19	02:30 PM	04:30 PM	WET
06/03/19	04:00 PM	04:05 PM	DRY


INSPECTION BY	ATTACHMENTS
MCDONALD-TAYLOR, H.	

COMMENTS

Material removal continued throughout the month. The company completed excavation of the ditch from Zone 1 to the building site in the vicinity of Zones 3 and 4. Since completion of the ditch the focus of material removal has been in the building zones. During the 6/19/19 inspection, the contractor had opened up a large pit in the vicinity of Zone 4. Solid ground was visible in the bottom of the pit, and pictures were taken to document that the contractor had excavated to solid at the building site. Heavy rains throughout the month has left the material saturated and much more difficult to work.

Photos of the site are shown below.

ABANDONED MINE LAND INSPECTION

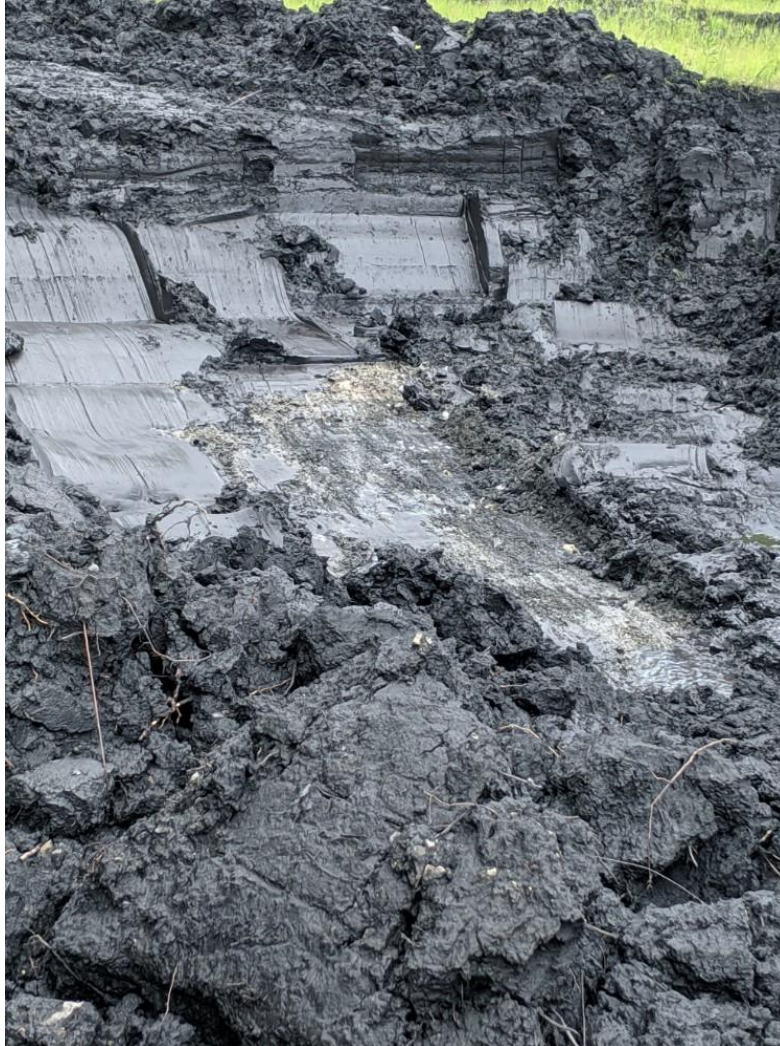

An area located at the building site that had been excavated to solid prior to backfill placement.

ABANDONED MINE LAND INSPECTION



Ditch construction from Zone 1 to Zone 3
